



Ideal Inspection

(a division of Ideal Oilfield Construction Ltd.)

P.O Box 1473

Brooks, Alberta

T1R 1C3

Phone: 403-362-2843

Fax: 403-362-2862

INSPECTION REPORT

Client: K&S Power Tongs	Location: DaPaJo Construction Limited	Date: May 10, 2013
P.O. :	Work Order : 2248g	Report : 3840
Page : 1 of 1	Unit : KS 710	S/N: 080490436
Inspection: Magnetic Particle		
Parts Examined: AOT 7" 65 Ton Side Door Casing Elevator		
Surface Condition: Painted	Material Temperature: 10° Celsius	
Procedure: MPI-DPJ-001	Code: ASME Section V, ASTM E709	
Equipment: Parker B 310 Contour Probe		
Method: Magnetic Particle, AC Continuous, Wet Florescent Method		
Test Medium: Magnaglow 14 HF Florescent Prepared Bath		


Test Results:

No defects were found at the time of this inspection.

Engineer's Approval:



Photos:

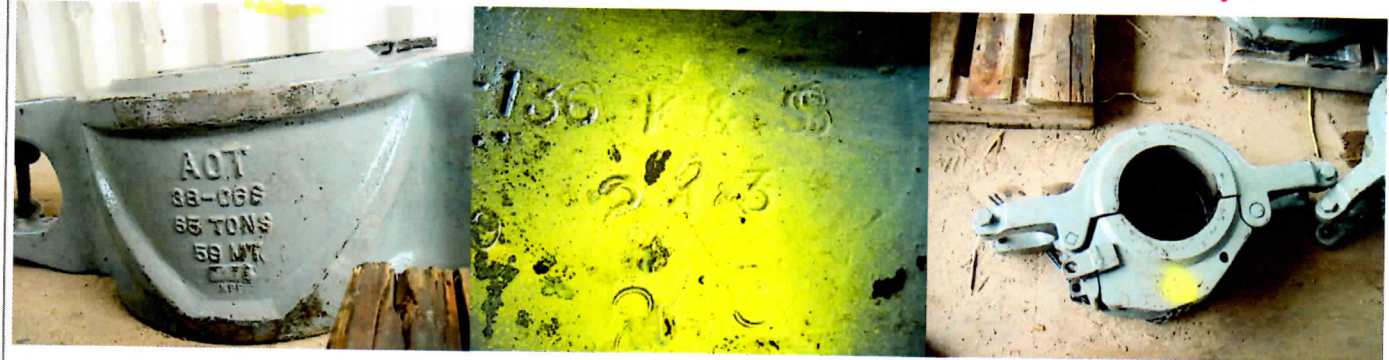

Technician:	John Frances	CGSB #:	7062	Signature:		Assistant:	Tyler Nevison			
Repairs Complete	Yes <input type="checkbox"/>	No <input type="checkbox"/>	N/A <input type="checkbox"/>	X <input checked="" type="checkbox"/>	Acceptable For Service			Yes <input type="checkbox"/>	X <input type="checkbox"/>	No <input type="checkbox"/>
